


# AIRPORT TRAIL TUNNEL




View of the tunnel formwork

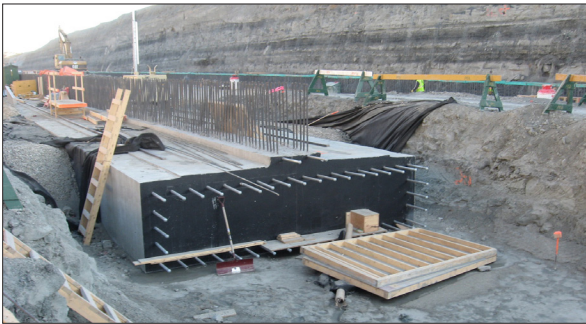

View of the central footing for the tunnel



View of the tunnel looking west

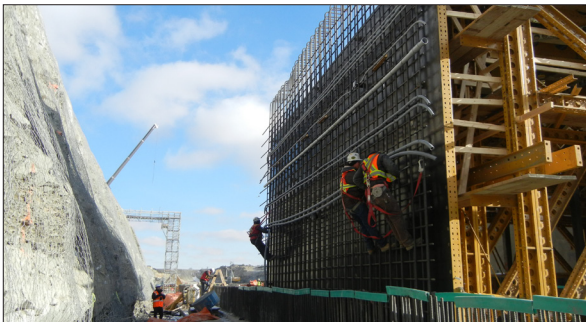

View of the exterior wall rebar and electrical conduit

## UPDATE 5 - FEBRUARY 2012

The tunnel excavation is now complete.

The tunnel footing formwork is well underway and approximately 250 metres of the footings have been formed. So far, approximately 3,000 m<sup>3</sup> out of the total 11,000 m<sup>3</sup> of concrete has been poured for the footings.

Crews are also continuing with the assembly and installation of forms for the tunnel walls and roof. They started to place both the north and south cell formwork into the tunnel on January 11 and February 1, consecutively. Approximately 25 metres of the total 620 metres of tunnel forms have been installed.

Crews started installing rebar and reinforcement for the tunnel walls and roof on February 2. Electrical conduits have also been placed on the exterior walls. It is anticipated that the concrete pour of the tunnel walls and roof slab will commence in late February.

Installation of underground utilities is nearing completion and over 500 metres of utilities have been completed.

### *DID YOU KNOW?*

*A total of 10,000,000 kg of rebar will be installed for the tunnel.  
450,000 kg of that has been installed to date.*
